



FOWLERVILLE COMMUNITY SCHOOLS



Fowlerville K-2 Elementary: Project Activities

- BCC and BFS has approved all disciplines.
- Interior flatwork will be completed in the building by mid-April.
- Interior brick and entryway masonry continues around the building. Door frame install is in progress.
- Window install began in mid-February and continues around the building.
- Consumer's Energy installed their gas lines and service is now on.
- DTE installed the meter for service to the building.
- Water main install began and will be completed by mid-April.
- All long lead items appear to still be on track. Boilers, pumps, RTUs, and VUVs have been received.
Lead times are updated weekly and are reflected in the construction schedule.

Schedule Status – Look Ahead:

- Interior wall framing continues around the building. Drywall to begin in the beginning of April.
- VUVs and RTUs to be set in the beginning of April.
- Duct, HVAC piping, interior plumbing and electrical continues around the building.
- Block filler continues around the building.

HVAC Project Planning:

- The High School and Junior High HVAC project documents were issued for bids on January 10, 2024
- The pre-bid meetings for both the High School and Junior High were held on January 17, 2024.
- Bids for the pre-purchase of the High School chillers, chiller pumps, and VFDs were due on February 13, 2024. The remainder of the project will be bid at a later date due to re-design. The target for the HVAC work is Summer 2025.
- The bid opening for the Junior High took place at the Junior High media center on March 13, 2024.
- The Junior High HVAC proposal will be re-bid at a later date due to budget limitations. The target for the HVAC work is Summer 2025.

Project Progress Photographs



VUV base install in progress.



VUV Rear extension and base installed.



Louvers staged for install.



Bird screen install at louver.

Project Progress Photographs



PVC water main material.




Water main install in progress.

Project Progress Photographs



Masonry wall in progress on top of interior slab.

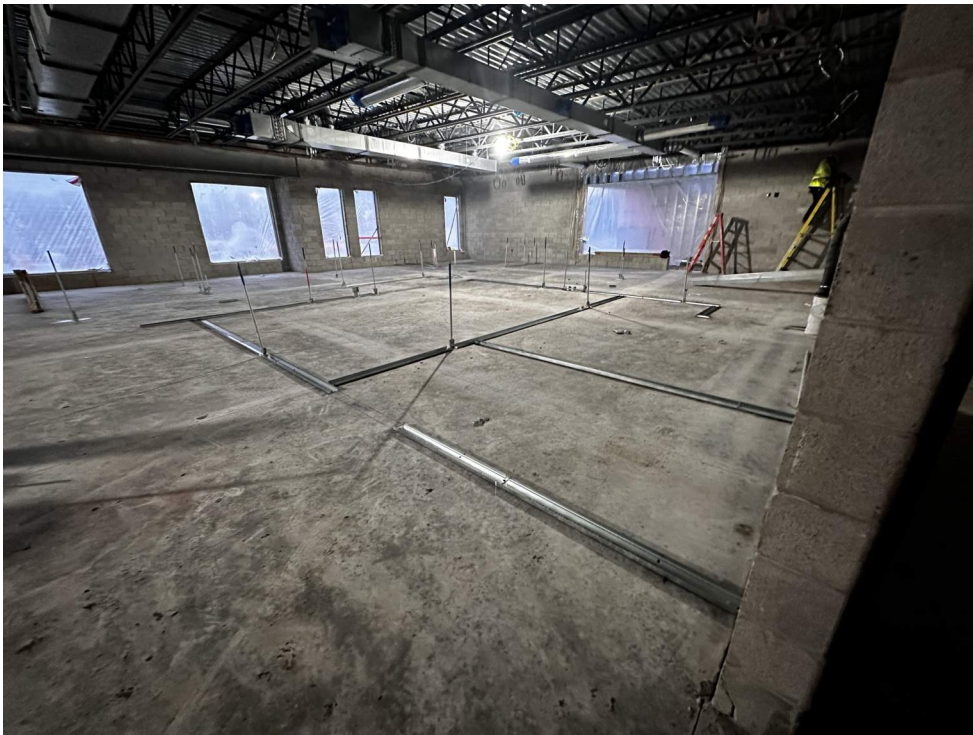

Layout for drywall framing.

Project Progress Photographs



Vapor barrier prep in gym prior to concrete pour.




Vapor barrier prep in the main office prior to concrete pour.

Project Progress Photographs



Concrete drying in hallway on east side of building.

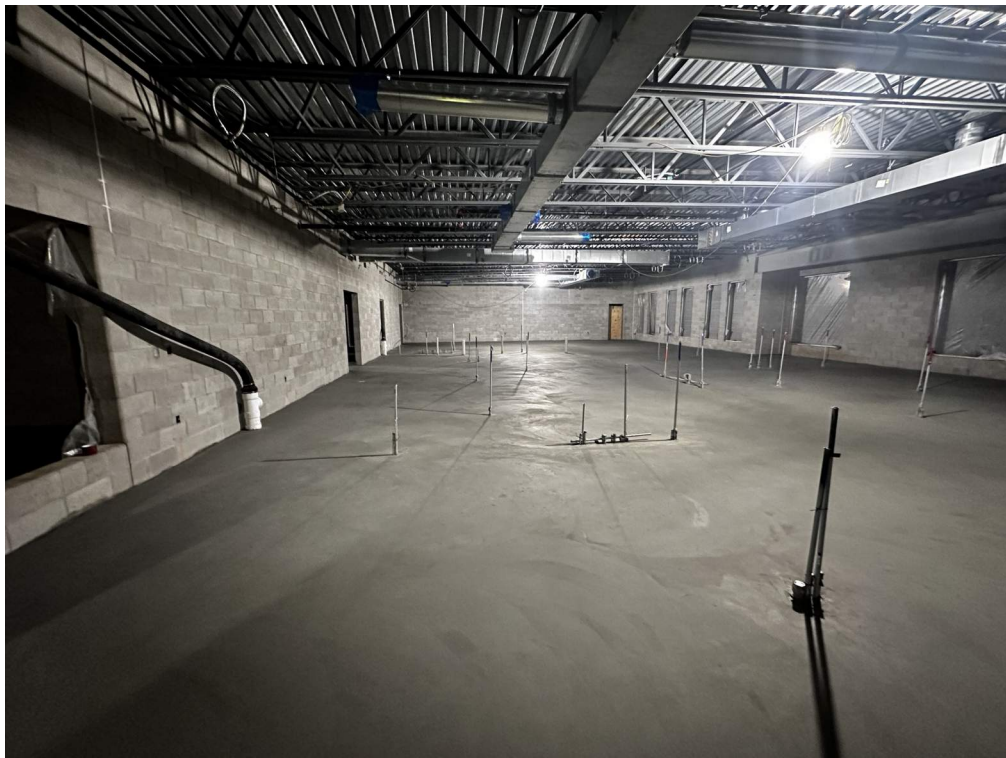

Concrete drying in classrooms on east side of building.
