



# FOWLERVILLE COMMUNITY SCHOOLS



## **Fowlerville K-2 Elementary: Project Activities**

- Overhead HVAC, plumbing, and electrical continues around the building.
- Vestibule frame and door install is complete. The building is secure.
- Drywall soffits began on the west and east sides of the building.
- Painting of ceilings and door frames continued around the building.
- Casework and solid surface install continued as well as markerboard and tackboard install.
- Classroom speaker install and wiring began on the west side of the building.
- Classroom flooring was completed on the west side and began on the east side.
- Spiral duct install was completed in the gym and cafeteria.
- Classroom light install began on the west side.
- Classroom millwork bench install began on the west side and continued to the east side.
- Concrete stabilization was completed at the bus lot.
- The water main connection was made on the north side of the site to bring water to the building.

## **Schedule Status – Look Ahead:**

- Locker install to begin mid-July.
- Switchgear install and communications cabling to begin at the beginning of July.

## **HVAC Project Planning:**

- Submittals for the pre-purchase of the High School chillers, chiller pumps, and VFDs were approved. The chillers are to be delivered in October 2024 and stored until Summer 2025 install.
- The High School and Junior High HVAC projects will be bid out in mid-August 2024 and bids will be due in early September 2024. The target for the HVAC work is Summer 2025.


## **Bond Planning:**

- Smith and Kreeger scopes are under review. The projects will be bid out in mid-September 2024 and bids will be due in early October 2024.


## Project Progress Photographs



Soffit finishing outside of classroom.

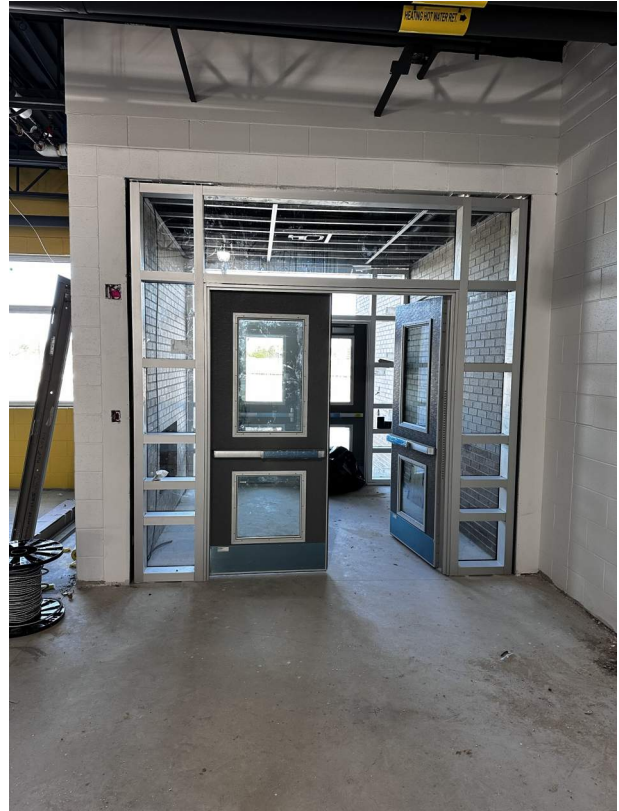

Vestibule door install on west side of building.

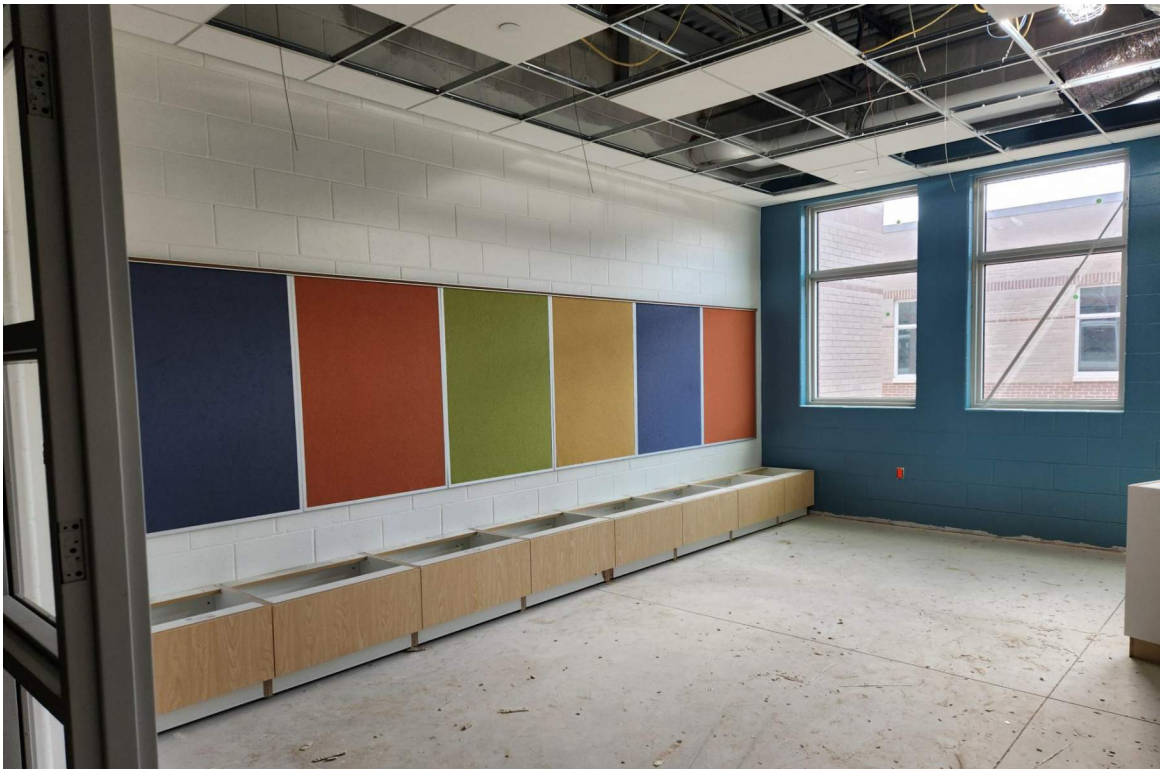

Tackboards and millwork benches in intervention area.

## Project Progress Photographs



Floor prep before flooring install.



LVT flooring installed in classroom.

## Project Progress Photographs



Light and speaker install in classroom.



Tack board and marker board install in classroom.

## Project Progress Photographs



Casework in office workroom.




Casework and passthrough cubbies in main office.

## Project Progress Photographs



Bench install at window of classroom.

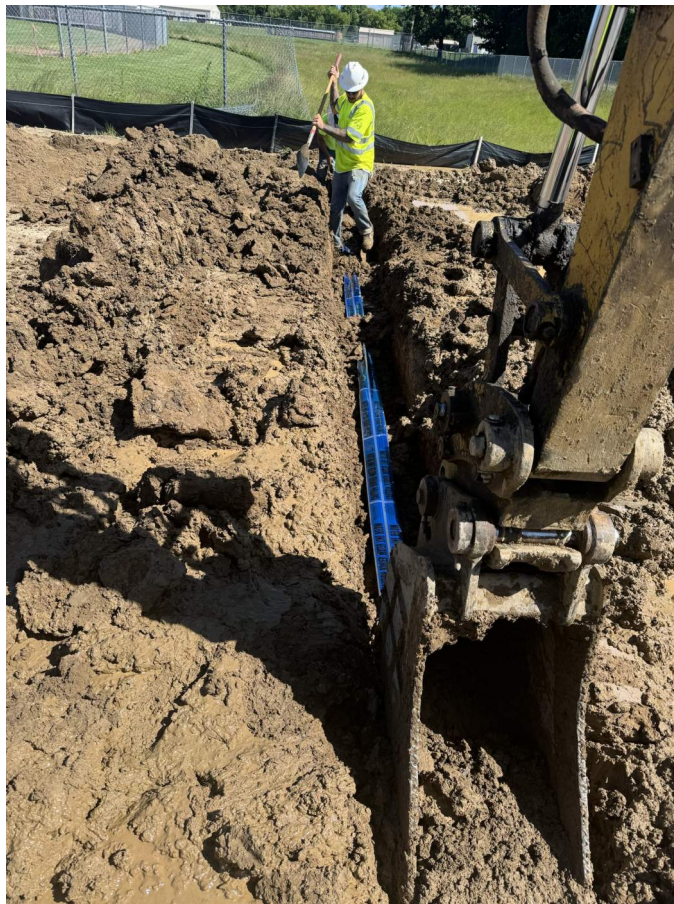

Warning tape install above water main.

## Project Progress Photographs



North water connection being made.



Light poles installed along bus lot drive on west side.
